

GPI: Gracias Por Invitar Budget Summary

Team: 9 Slice: Event-goer features (7 stories, 37 points, 71 FP) Date: 10/06/2026, from the budget dated 10/04/2026 Status: **Final**

603.67 h

Planning value: PERT expected effort

\$58,868

Total budget request, both reserves included


12.1 weeks

Expected duration at 50 team-hours a week

Cost-driving assumptions and owners

Cost-driving assumption	Owner
Slice boundary. Only the event-goer slice is priced: 7 stories, 37 points, 71 function points. Imports from outside sources are excluded; one import adds about 12 FP (108 h).	Emmanuel Saenz, Project Manager
Event supply. Organizers post into a GPI catalogue that the team curates, as the charter and business strategy set out. No imported feeds in the build.	Oscar Vargas, Business Strategy Lead
Team capacity. Five people at 10 productive hours a week (50 team-hours) alongside coursework. Project management at 0.15 FTE (58.5 h) sits inside the 603.67 h.	Jazmin Huerta, Market Research Lead
Estimation rates. 6 to 12 h per function point; analogous at 70 h per person-month, 50 to 70 percent match, 25 to 35 percent uplift. None measured; replaced after three sprints.	Christian Lopez, Research Documentation Lead
Labor and hosting price. \$82.18 per productive hour from a \$51.36 hourly base (ZipRecruiter), a 1.20 burden and 130 productive hours a month. Tools and hosting on free tiers.	Samuel Alderete, Portal Lead

Effort: two methods and the planning value

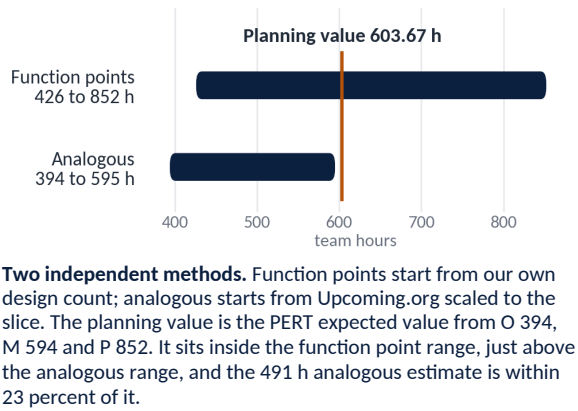

Staffing by role and month

Role	M1	M2	M3	FTE-months
Project manager	0.15	0.15	0.15	0.45
Developers	1.01	1.07	0.65	2.73
Quality assurance	0.08	0.26	0.37	0.71
User experience	0.28	0.14	0.00	0.42
DevOps	0.15	0.05	0.14	0.34
Total FTE	1.67	1.67	1.31	4.64

Months are rounded; unrounded totals of 1.667, 1.667 and 1.310 sum to 4.64. Months 4 to 6 carry no staff.

Why the shape

Each month is capped at 1.67 FTE: five people at 10 productive hours a week. UX front-loads the account, category and calendar screens. QA peaks in Month 3 for end-to-end testing. DevOps peaks at environment setup in Month 1 and deployment in Month 3. Month 3 is lighter because only about 0.8 of a month of work remains.

At 130 productive hours per FTE-month, 603.67 h is 4.64 FTE-months of effort, spread over about 12.1 calendar weeks at the team's part-time pace.

Budget stack

Budget line	Amount
Labor: 603.67 h (4.64 FTE-months) at \$82.18 per productive hour	\$49,607
Non-labor: domain name; everything else on free tiers	\$15
Base build estimate	\$49,622
+ Contingency reserve: EMV of three named risks	\$6,443
Cost baseline	\$56,065
+ Management reserve: 5 percent of the baseline	\$2,803
Total budget request	\$58,868
Annual operating cost, a separate line: support at 5 team-hours a week, plus the domain	\$21,381 / yr

Contingency sits inside the baseline and is controlled by the project manager. Management reserve sits outside it and is held by the sponsor for surprises nobody has named.

Top risks and the schedule gap

Top risk	Chance	Impact	EMV
Effort lands near the pessimistic 852 h (+248 h); our rates are not yet measured	15%	\$20,407	\$3,061
Organizers do not post, so the team imports outside events (108 h)	30%	\$8,875	\$2,663
Uneven El Paso and Juárez event data needs a cleanup pass (35 h)	25%	\$2,876	\$719
Contingency reserve			\$6,443

Cross-check: one PERT spread of effort risk alone is 76.33 h × \$82.18 = \$6,273. The reserve covers it with \$170 to spare.

Schedule gap

The charter's top-down number is 8 weeks at 50 team-hours: 400 h, about \$32,870 of labor. The bottom-up slice prices at 603.67 h and \$49,607, which is 203.67 h or about 51 percent more, and takes roughly 12.1 weeks at the same pace. Closing the gap means a smaller slice or a longer timeline.

Sources: GPI Session 11 Part 1 Budget, Steps 1 to 10 (the 11-page support document); budget figures are the final Step 10 values. Wage base: [ZipRecruiter](#), [IT software engineer salary in Texas](#). Analogous base: Upcoming.org history, sourced in the team's Session 9 estimation. Every other chosen number is a team assumption with the owner shown.

Team sign-off: Team 9 approved all four items as written: the five assumptions and owners; the staffing split by month; the three risk chances and impacts; and the 5 percent management reserve.
