GRACIAS POR INVITAR, LIVING PROJECT PORTAL, SPRINT 2

Project Budget

The team's budget for the event-goer slice: the one-page summary a sponsor reads (603.67 hours, $58,868 requested, 12.1 weeks) and the ten steps behind it, from five cost-driving assumptions with owners through the staffing plan, labor at loaded cost and productive hours, a base build of $49,622 and two reserves to the time-phased request.

Version	1.3, Final, revised Oct 5, 2026
Owner	Emmanuel Saenz
Team	Samuel Alderete, Jazmin Huerta, Christian Lopez-Matulessy, Emmanuel Saenz, Oscar Vargas
Course	CS 4390/5388 Software Project Management, The University of Texas at El Paso, Fall 2026
Web	https://gpi-portal.onrender.com/sprint-2/budget/

What this document is

The course's Session 11 activity, "Building the Budget", turns an estimate into money in ten steps: the assumptions the cost depends on, the work in packages, effort from more than one method, hours converted to FTE-months, a staffing plan by month, a loaded labor rate, the labor and everything else, the cost of ownership, the risks and the two reserves, and the budget time-phased into a request. The team's budget starts from the Estimation Appendix: the range of 394 to 852 hours for the event-goer slice, and the planning value of 603.67 hours.

This page carries the two documents the team delivered, as the team wrote them. First the one-page budget summary of 6 October 2026, the version a sponsor reads. Then the ten-step budget of 4 October 2026 that supports it, step by step. The files are the Team's PDFs above. The charts are redrawn from the team's figures in the portal's palette, so they read in both themes and in print, and the revision history at the foot of the page records where the page and the delivered files differ.

TEAM	9, Gracias Por Invitar
PROJECT	GPI: Gracias Por Invitar
SLICE	Event-goer features (7 stories, 37 points, 71 FP)
BUDGET	Session 11, Part 1: Building the Budget, 4 October 2026
SUMMARY	One-page budget summary, 6 October 2026

STATUS	Final

The budget on one page

603.67 h
Planning value: PERT expected effort


$58,868
Total budget request, both reserves included

12.1 weeks
Expected duration at 50 team-hours a week

Cost-driving assumptions and owners

COST-DRIVING ASSUMPTION	OWNER
Slice boundary. Only the event-goer slice is priced: 7 stories, 37 points, 71 function points. Imports from outside sources are excluded; one import adds about 12 FP (108 h).	Emmanuel Saenz, Project Manager
Event supply. Organizers post into a GPI catalogue that the team curates, as the charter and business strategy set out. No imported feeds in the build.	Oscar Vargas, Business Strategy Lead
Team capacity. Five people at 10 productive hours a week (50 team-hours) alongside coursework. Project management at 0.15 FTE (58.5 h) sits inside the 603.67 h.	Jazmin Huerta, Market Research Lead
Estimation rates. 6 to 12 h per function point; analogous at 70 h per person-month, 50 to 70 percent match, 25 to 35 percent uplift. None measured; replaced after three sprints.	Christian Lopez, Research Documentation Lead
Labor and hosting price. $82.18 per productive hour from a $51.36 hourly base (ZipRecruiter), a 1.20 burden and 130 productive hours a month. Tools and hosting on free tiers.	Samuel Alderete, Portal Lead

Effort: two methods and the planning value

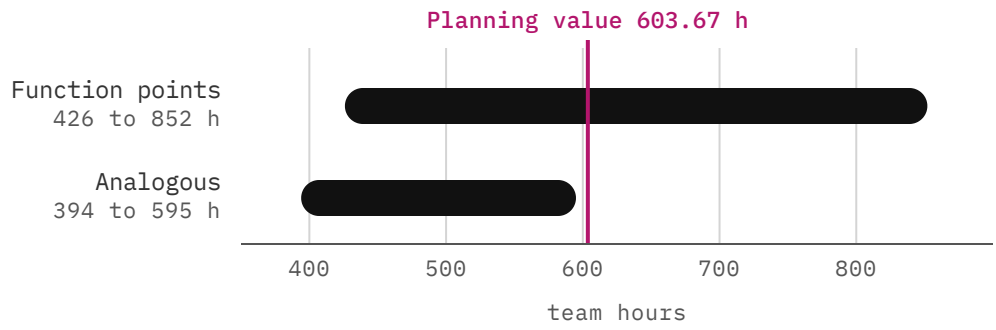

Effort, two methods and the planning value: function points give 426 to 852 hours, the analogous method 394 to 595 hours, and the PERT planning value of 603.67 hours sits inside the first range, just above the second.

Two independent methods. Function points start from our own design count; analogous starts from Upcoming.org scaled to the slice. The planning value is the PERT expected value from O 394, M 594 and P 852. It sits inside the function point range, just above the analogous range, and the 491 h analogous estimate is within 23 percent of it.

Staffing by role and month

ROLE	M1	M2	M3	FTE-MONTHS
Project manager	0.15	0.15	0.15	0.45
Developers	1.01	1.07	0.65	2.73
Quality assurance	0.08	0.26	0.37	0.71
User experience	0.28	0.14	0.00	0.42
DevOps	0.15	0.05	0.14	0.34
Total FTE	**1.67**	**1.67**	**1.31**	**4.64**

Months are rounded; unrounded totals of 1.667, 1.667 and 1.310 sum to 4.64. Months 4 to 6 carry no staff.

WHY THE SHAPE

Each month is capped at 1.67 FTE: five people at 10 productive hours a week. UX front-loads the account, category and calendar screens. QA peaks in Month 3 for end-to-end testing. DevOps peaks at environment setup in Month 1 and deployment in Month 3. Month 3 is lighter because only about 0.8 of a month of work remains.

At 130 productive hours per FTE-month, 603.67 h is 4.64 FTE-months of effort, spread over about 12.1 calendar weeks at the team's part-time pace.

Budget stack

BUDGET LINE	AMOUNT
Labor: 603.67 h (4.64 FTE-months) at $82.18 per productive hour	$49,607
Non-labor: domain name; everything else on free tiers	$15
Base build estimate	**$49,622**
+ Contingency reserve: EMV of three named risks	$6,443
Cost baseline	**$56,065**
+ Management reserve: 5 percent of the baseline	$2,803
Total budget request	**$58,868**
Annual operating cost, a separate line: support at 5 team-hours a week, plus the domain	$21,381 a year

Contingency sits inside the baseline and is controlled by the project manager. Management reserve sits outside it and is held by the sponsor for surprises nobody has named.

Top risks and the schedule gap

TOP RISK	CHANCE	IMPACT	EMV
Effort lands near the pessimistic 852 h (+248 h); our rates are not yet measured	15%	$20,407	$3,061
Organizers do not post, so the team imports outside events (108 h)	30%	$8,875	$2,663
Uneven El Paso and Juárez event data needs a cleanup pass (35 h)	25%	$2,876	$719
Contingency reserve			**$6,443**

Cross-check: one PERT spread of effort risk alone is 76.33 h × $82.18 = $6,273. The reserve covers it with $170 to spare.

SCHEDULE GAP

The charter's top-down number is 8 weeks at 50 team-hours: 400 h, about $32,870 of labor. The bottom-up slice prices at 603.67 h and $49,607, which is 203.67 h or about 51 percent more, and takes roughly 12.1 weeks at the same pace. Closing the gap means a smaller slice or a longer timeline.

Sources and sign-off

Sources: GPI Session 11 Part 1 Budget, Steps 1 to 10 (the 11-page support document); budget figures are the final Step 10 values. Wage base: ZipRecruiter, IT software engineer salary in Texas. Analogous base: Upcoming.org history, sourced in the team's Session 9 estimation. Every other chosen number is a team assumption with the owner shown.

Team sign-off: Team 9 approved all four items as written: the five assumptions and owners; the staffing split by month; the three risk chances and impacts; and the 5 percent management reserve.

The ten steps behind it

The support document: the team's completed "Building the Budget" activity of 4 October 2026, carried step by step as the team wrote it. The summary above takes its figures from the final Step 10 values.

Estimate, budget, baseline

Three different things. The Session 9 estimate becomes a budget only when someone with authority approves it, and the baseline is the version the team is held to.

	ESTIMATE	BUDGET	COST BASELINE
What it is	A forecast of effort and cost, with a range	The money leadership approves, including a cushion for surprises	The approved month-by-month spending plan you measure against

	ESTIMATE	BUDGET	COST BASELINE
Set by	The project team	The sponsor (the executive who pays)	Built by the project manager, approved by the sponsor
GPI	394 to 852 hours = $32,377 to $70,014. Expected 603.67 hours = $49,607 (traced to Step 3 in this document)	Requested: $58,868. Baseline: $56,065. Cushion: $2,803 (Step 10)	$56,065: the $49,622 base build phased over 3 months (M1 $17,820, M2 $17,805, M3 $13,997), plus $6,443 contingency held back for named risks (Step 10)

Two ways to start a budget

	TOP-DOWN	BOTTOM-UP
How it starts	From a number someone wants, such as a fixed date or a fixed dollar amount.	From the list of work that has to be done, priced piece by piece.
GPI	Project Charter: 8 weeks × 50 team-hours = 400 hours × $82.18 (per productive hour) ≈ $32,870	Seven work packages (37 points, 71 function points): 603.67 hours, $49,607 of labor plus $15 non-labor = $49,622
Use it for	A quick reality check. It tells you what leadership hopes for.	The budget you defend. It tells you what the work costs.

Build bottom-up, then set it beside the top-down number. The gap between the two is a finding, written up in Check 5 under Step 10.

Step 1: what the cost depends on

A cost-driving assumption is a statement that, if it turned out wrong, would change the cost. The team lists five, each with an owner.

ASSUMPTION	WHY IT DRIVES COST	OWNER
In the event-goer slice, we include 7 stories, which are 37 points and 71 function points. Any outside-source imports are out.	Everything outside the slice is unpriced. An import is 12 function points which equals about 108 hours.	Emmanuel Saenz, Project Manager (charter scope)

ASSUMPTION	WHY IT DRIVES COST	OWNER
Organizers post events into GPI-created catalogue, and the team curates it first, like how the charter and Business Strategy have it.	Rules out imported work in the build and sets the curation hours in the operating cost.	Oscar Vargas, Business Strategy Lead
Five people contributing 10 productive hours a week each, 50 team-hours a week, alongside coursework, for the whole build. Delivery work is split across developer, QA, UX and DevOps roles (65/17/10/8 percent, 545.17 delivery hours), and project management at 0.15 FTE is carved out of the 603.67 hours (58.5 hours). See the notes below.	Sets the 12.1-week expectation and the monthly spend. Fewer hours contributed extends the calendar, but total hours remain the same. Pricing project management on top would add about 58.5 hours ($4,807).	Jazmin Huerta, Market Research Lead
6 to 12 hours per function point, 70 hours per person-month for the comparable, with a 50 to 70 percent match and a 25 to 35 percent uplift. We have not measured any of these yet.	Our whole range depends on these. After three sprints we'll replace them with our real numbers.	Christian Lopez, Research Documentation Lead (Appendix owner)
Labor at $51.36 an hour (ZipRecruiter) = $106,829 a year. × 1.20 burden = $10,683 per FTE-month, or $82.18 per productive hour. Tools and hosting stay on free tiers, since the charter has no money for paid licenses. See the notes below.	Every dollar amount is the number of hours times this rate. A 1.4 burden would push labor up 17 percent, and paying to host the app would add a new cost.	Samuel Alderete, Portal Lead

NOTES TO ROWS 3 AND 5

The 65/17/10/8 percentages are shares of the delivery hours (545.17), not of the full 603.67. The 0.15 is an FTE figure, not a percentage of hours. It means 15% of one full-time person each month, which is 0.15 × 130 = 19.5 hours a month, or 58.5 hours over 3 months. This is how the hours are carved out:


1. Start with the total: 603.67 hours.
2. Take the PM's share off first: 603.67 − 58.5 = 545.17 hours left for delivery.
3. Split those 545.17 hours 65/17/10/8 among the delivery roles.

The Session 9 estimate priced hours at $61.63, a loaded rate per paid hour; this budget prices them per productive hour, $82.18.

Step 2: the work in packages

WORK PACKAGE	ROLE	HOURS
Unified El Paso-Juárez calendar (8 pts)	Developers, UX, QA, DevOps (environment setup)	117.9
Upcoming events by date (5 pts)	Developers, UX, QA	73.7
Event time, place and details (3 pts)	Developers, UX, QA	44.2
Account and event categories (8 pts)	Developers, UX, QA	117.9
Feed ranked to categories (5 pts)	Developers, QA	73.7
Saving an event (3 pts)	Developers, QA	44.2
Search by name or keyword (5 pts)	Developers, QA, DevOps (deployment)	73.7
Project management (all packages)	Project manager (PM)	58.5
Total delivery effort	37 pts × 14.73 hrs + 58.5 PM	**603.67**

The rate becomes 545.17 ÷ 37 = 14.73 hours per point, because 58.5 of the 603.67 hours go to project management first.

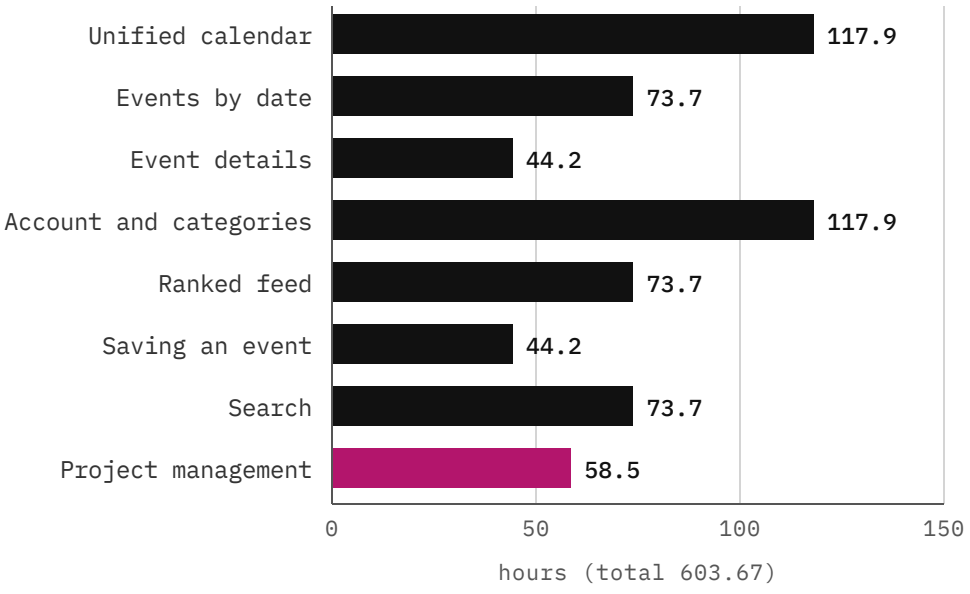

Hours by package: the seven packages at 14.73 hours per story point and the 58.5 project management hours carved out first, 603.67 hours in all.

Step 3: effort more than one way


Three-point (PERT)

E = (O + 4M + P) ÷ 6. O, the optimistic case, is 394 hours, if everything goes well. M, the most likely, is 594 hours. P, the pessimistic case, is 852 hours, if real problems hit. E = 3,622 ÷ 6 = 603.67 hours.

Why E is above M: the bad case is farther from most likely than the good case is, so it pulls the answer up. Spread = (P − O) ÷ 6 = (852 − 394) ÷ 6 = 76.33 hours: a typical miss. Step 9 reuses it.

The methods side by side

METHOD	HOURS	WHAT IT STARTS FROM
Bottom-up (the packages)	603.67	The seven work packages in Step 2 at 14.73 hours per story point across 37 points, plus 58.5 project management hours. The package hours were distributed from the PERT expected value, so this line is not an independent check on PERT.
Three-point (PERT)	603.67	O 394 from the analogous low. P 852 from 71 function points at 12 hours each. M 594 from the midpoint of the two method ranges (623) and the midpoint of their two middles (565).
Analogous	491	Upcoming.org: one person over about 9 months at an assumed 70 hours per person-month, so 630 hours, scaled by a 50 to 70 percent feature match and a 25 to 35 percent coordination uplift. Range 394 to 595.
Planning value	**603.67**	The PERT expected value, which the bottom-up packages plus project management also sum to. This is the number carried into Step 4.

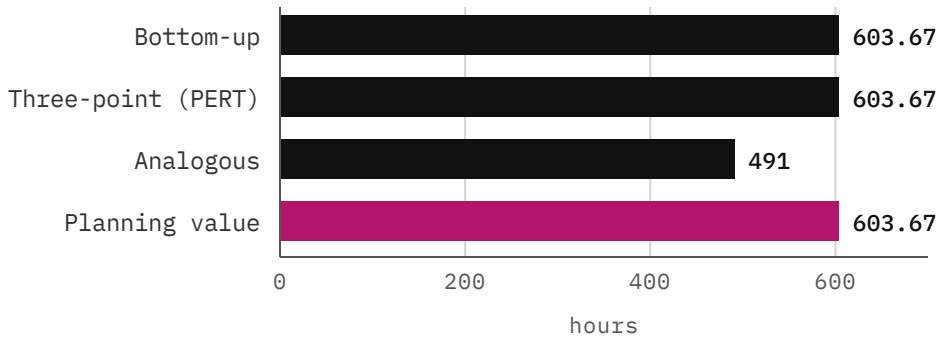

Effort estimates in hours. Bottom-up and PERT are the same number by construction; the analogous estimate is the independent comparison. The planning value is 603.67 hours.


Do the methods land within 25 percent of each other? The rule of thumb: if they differ by more than 25 percent, find out why before pricing anything. The team's answer: not needed, the spread is

23 percent. The planning value of 603.67 hours sits 22.9 percent above the 491 hour analogous midpoint, inside the 25 percent rule. Bottom-up and PERT are identical because the package hours were distributed from the PERT expected value, so analogous is the only independent comparison in the table.

Step 4: hours to FTE-months

ROLE	HOURS	FTE-MONTHS (HOURS ÷ 130)
Developers	354.4	2.73
Quality Assurance (QA)	92.7	0.71
User Experience (UX)	54.5	0.42
DevOps	43.6	0.34
Delivery subtotal	545.17	4.19
Project manager (0.15 × 3 months)	58.5	0.45
Total	**603.67**	**4.64**

How to read it: one FTE-month is one person working full time for one month. About 80 percent of a month (130 of 160 hours) is productive project time; the rest goes to meetings, email, support and time off. The rate the team assumed: 130 productive hours per FTE-month.

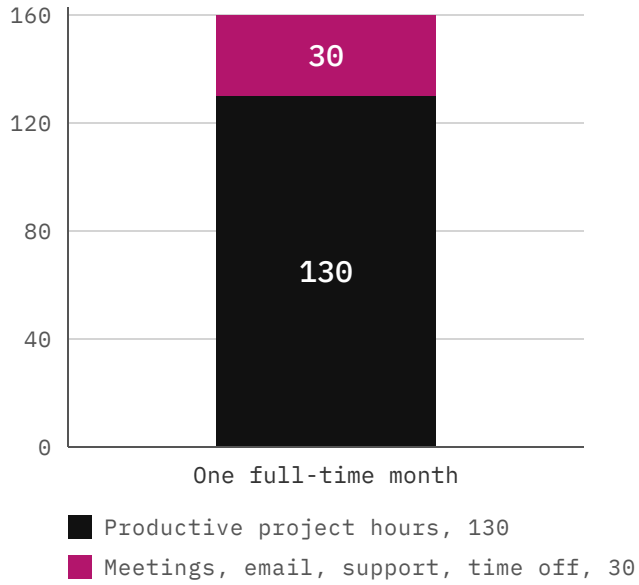

One full-time month: 160 nominal hours, of which 130 are productive project hours and 30 go to meetings, email, support and time off.

At 130 productive hours per FTE-month, 603.67 hours is 4.64 FTE-months of work. Our own Step 1 assumption is 10 productive hours per person per week, which is 50 team-hours a week, so those 4.64 FTE-months spread across about 12.1 weeks of calendar time. The role rows are rounded to two decimals; the total of 4.64 is taken from the unrounded values.

Any of our five members may fill the defined roles. Delivery hours are split by 65 percent developers, 17 percent QA, 10 percent UX and 8 percent DevOps, a team assumption owned by Jazmin Huerta (Step 1, row 3). Project management is priced at 0.15 FTE for 3 months, about 4.5 hours a week, and is carved out of the 603.67-hour planning value.

Step 5: the staffing plan by month

ROLE	M1	M2	M3	M4	M5	M6	FTE-MONTHS
Project manager	0.15	0.15	0.15	0	0	0	0.45
Developers	1.01	1.07	0.65	0	0	0	2.73
Quality assurance	0.08	0.26	0.37	0	0	0	0.71
User experience	0.28	0.14	0	0	0	0	0.42

ROLE	M1	M2	M3	M4	M5	M6	FTE-MONTHS
DevOps	0.15	0.05	0.14	0	0	0	0.34
Total FTE	**1.67**	**1.67**	**1.31**	0	0	0	**4.64**

Why the shape

- For the UX, we have more hours dedicated to it in the beginning because the account, category, and calendar screens are designed first.
- QA rises as features are finished and peaks in Month 3 for end-to-end testing.
- DevOps peaks when the environment is set up in Month 1 and deployment in Month 3.
- Developers carry out most of the work throughout, and the project manager keeps a steady 0.15 FTE.
- Each month is capped at our capacity of 1.67 FTE (five people at 10 productive hours a week, 0.33 FTE each) and Month 3 is lighter because only about 0.8 of a month of work remains.

Check the total

All roles total 4.64 FTE-months, the same as Step 4's FTE-months.

Step 6: the loaded labor rate

$106,829
blended base salary a year ($51.36 × 2,080 hours)

$8,902
a month (÷ 12)

× 1.2
burden factor

$10,683
per FTE-month

What is burden? Costs an employer pays on top of salary: benefits, payroll taxes, equipment and workspace. Commonly used factors run about 1.25 to 1.4. The 1.20 burden is a team assumption, below the 1.25 to 1.4 common range.

RATE	VALUE
Per nominal hour (÷ 160)	$66.77
Per productive hour (÷ 130)	$82.18

Pricing at the nominal-hour rate understates labor, because only 130 of 160 hours are productive.

Steps 6 and 7 worked: price the labor and everything else

Labor: FTE-months × $10,683

ROLE	FTE-MONTHS	COST
Project manager	0.45	$4,807
Developers	2.73	$29,120
Quality assurance	0.71	$7,616
User experience	0.42	$4,480
DevOps	0.34	$3,584
Labor total	**4.64**	**$49,607**

Non-labor: everything else you buy

ITEM	HOW COMPUTED	COST
Hosting: web service and database	Free tier during the build and the pilot (charter: no budget for paid licenses). A small tier would be about $25 a month, an assumption to price from the vendor's published rates.	$0
Domain name	One year, assumption	$15
Transactional email for sign-up	Free tier at pilot volumes	$0
Maps or geocoding for event places	Free tier at pilot volumes	$0
Repository, CI, design tools	Free tiers	$0
Organizer onboarding materials	Digital only: labor, not a purchase	$0

ITEM	HOW COMPUTED	COST
Non-labor total		**$15**


Base build estimate: $49,607 labor + $15 non-labor = $49,622.

Step 8: the cost of ownership

The build ends, but the system keeps costing money. It has to be hosted, fixed and supported every year.

ANNUAL OPERATING COST	HOW IT WAS COMPUTED	PER YEAR
Support and maintenance	5 team-hours a week × 52 × $82.18	$21,366
Production hosting	Free tier plus the domain	$15
Licenses and services	Free tiers	$0
Operating total	Sum of annual operation items	**$21,381**

Why it belongs in the budget: over 1 year, operating cost ($21,381) compared to the build ($49,622). Total cost of ownership is $71,003.



Base cost over the horizon: the $49,622 build and $21,381 a year of operating cost. Total cost of ownership for one year, $71,003.


Step 9: the risks and the two reserves

Price the risks: the contingency reserve

RISK	CHANCE	IMPACT	EMV
Effort lands near the pessimistic 852 hrs; our rates are not measured yet (+248.33 hrs)	15%	$20,407	$3,061
Organizers don't post, so we import events from outside sources (108 hrs)	30%	$8,875	$2,663
Uneven El Paso-Juárez event data needs a cleanup and review pass (35 hrs)	25%	$2,876	$719
Contingency reserve			**$6,443**

How to read it: expected monetary value (EMV) = chance × impact. It is an average, not a prediction: a risk either costs about its impact or nothing, and the reserve covers the expected total. The template asks for the top three risks at least.

Cross-check: one PERT spread from Step 3 × the productive-hour rate = $6,273 (76.33 hrs × $82.18) of effort risk alone. Is the reserve at least that large? Yes, $6,443 is $170 more.

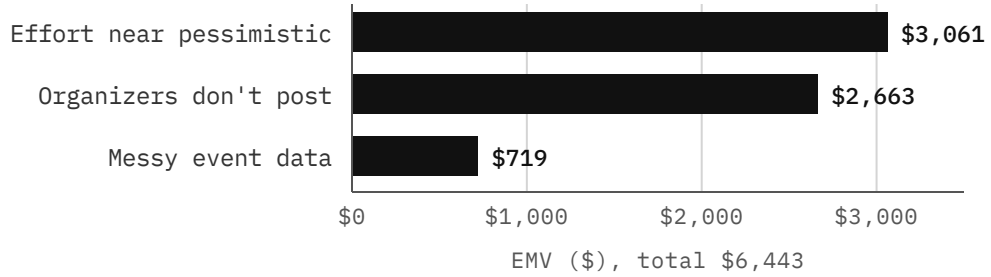

Expected monetary value by risk, chance times impact: $3,061, $2,663 and $719, a contingency reserve of $6,443.

Two reserves

	CONTINGENCY RESERVE	MANAGEMENT RESERVE
Covers	Risks you have named (known unknowns)	Surprises nobody has named (unknown unknowns)
Inside the cost baseline?	Yes	No

	CONTINGENCY RESERVE	MANAGEMENT RESERVE
Controlled by	Project manager	Sponsor or leadership
Sized by	The risk table (sum of EMV)	Organizational policy, here 5 percent
GPI	$6,443, contingency, inside the baseline	$2,803, management reserve: 5 percent of the $56,065 baseline

Baseline = base build + contingency: $56,065 = $49,622 + $6,443.

A NAMED RISK HAPPENS

Organizers don't post and the team has to import events (risk 2, about $8,875). The project manager spends contingency without asking.

A SURPRISE NOBODY LISTED


A teammate has to drop the course mid-build, and handing off their unfinished work costs hours nobody planned for. The project manager asks the sponsor to release management reserve.

Step 10: the budget, phased and requested

Time-phase the budget

MONTH	LABOR	NON-LABOR	TOTAL	CUMULATIVE
1	$17,805	$15	$17,820	$17,820
2	$17,805	$0	$17,805	$35,625
3	$13,997	$0	$13,997	$49,622
4	$0	$0	$0	$49,622
5	$0	$0	$0	$49,622
6	$0	$0	$0	$49,622

Time-phasing places each cost in the month it is spent. Labor = FTE that month × $10,683 per FTE-month (Step 6), using Step 5's unrounded FTE of 1.667, 1.667 and 1.310. The $15 domain is bought in month 1. Contingency is held back until a named risk occurs, so this shows the base build only.

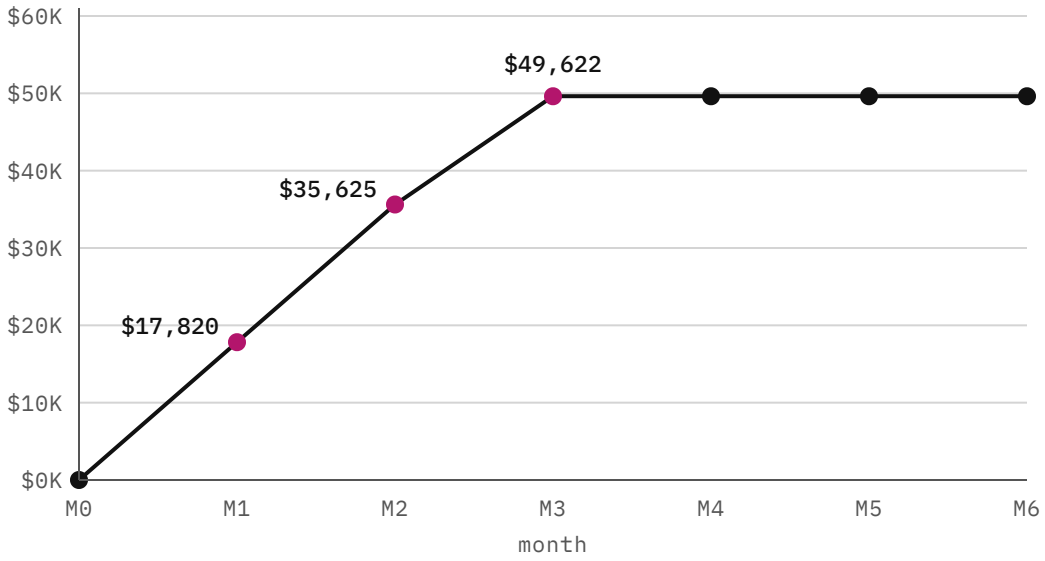


Cumulative base spend by month: $17,820 after month 1, $35,625 after month 2, and the full $49,622 base build by the end of month 3.

The full budget request

LINE	AMOUNT
Labor	$49,607
Non-labor	$15
Base build estimate	$49,622
Contingency reserve (EMV)	$6,443
Cost baseline	$56,065
Management reserve (5%)	$2,803
Total budget request	**$58,868**
Operating cost (separate line)	$21,381 a year

How to read it: each line stacks on the last. Base build is what you expect. Contingency covers named risks. Management reserve covers the unnamed.

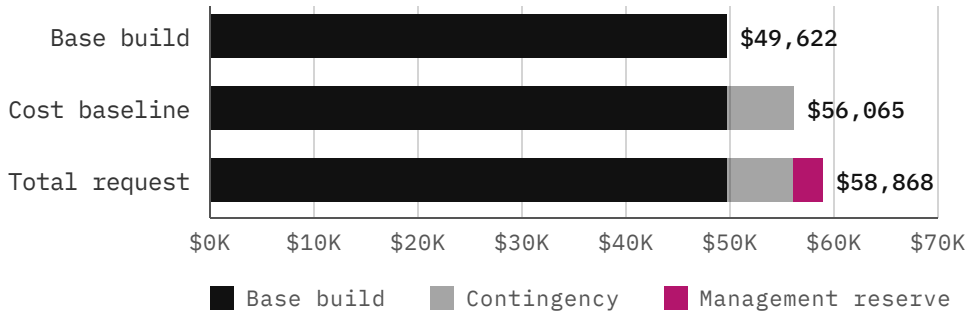


Building the request: the $49,622 base build, the $6,443 contingency that makes the $56,065 cost baseline, and the $2,803 management reserve that makes the $58,868 total request.

Five sanity checks


1. **Totals match.** Add the staffing plan by month and compare it to Step 4. Ours: 4.64 FTE-months by month (1.667 + 1.667 + 1.310) = 4.64 FTE-months in Step 4.
2. **Labor share is plausible.** Divide labor by the base build. Ours: $49,607 ÷ $49,622 = 99.97 percent. Nearly all cost is people because every tool and service stays on a free tier.
3. **Estimates agree.** Compare the effort estimates. Ours: 491 to 603.67 hours, within 23 percent.
4. **Reserves trace to risks.** Every contingency dollar links to a named risk in the Step 9 table. Ours: $3,061 + $2,663 + $719 = $6,443, all three named in the Step 9 table.
5. **Top-down comparison.** Put the sponsor's number next to yours and explain the gap. Sponsor's number: 400 hours (8 weeks × 50 team-hours), about $32,870 of labor. Ours: 603.67 hours, $49,607 of labor. The gap is 203.67 hours, or $16,737, about 51 percent more. Eight weeks at our 50 team-hours a week only fits 400 hours, but the seven stories in the slice price at 603.67 hours, which takes about 12.1 weeks at that pace. To close the gap either the slice gets smaller or the timeline gets longer.

Check 5 in action: the sponsor's number

What did the sponsor ask for, in time or money? 8 weeks at 50 team-hours a week, so 400 hours (about $32,870). Our budget says the work is 4.64 FTE-months.

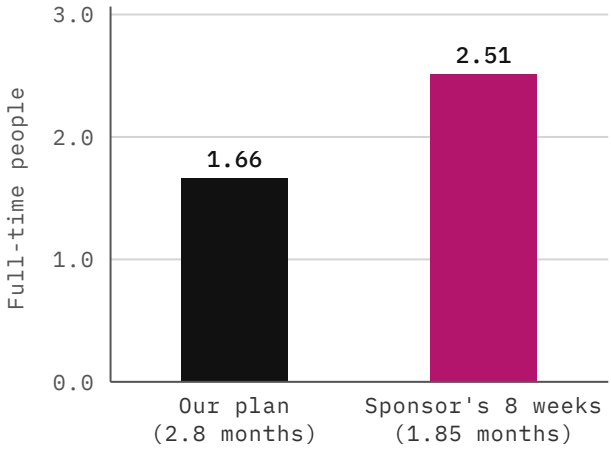

People needed for 4.64 FTE-months: 1.66 full-time people over the plan's 2.8 months, or 2.51 over the sponsor's 8 weeks (1.85 months).

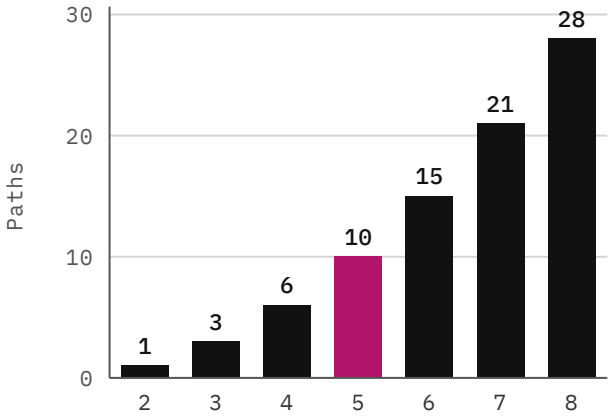

Communication paths, n(n − 1) ÷ 2: with five people there are ten pairs where a misunderstanding can happen.

4.64 FTE-months ÷ 2.8 months = 1.66 people. 4.64 FTE-months ÷ 1.85 months (the sponsor's time) = 2.51 people. Every pair of people is a path where a misunderstanding can happen. 5 people means 10 of them.

What is still open

- The rates behind every figure are assumed, not measured: hours per function point, hours per person-month for the comparable, the match and the uplift, the burden factor, and 130 productive hours per FTE-month. The team replaces them with its own numbers after three sprints, and the budget moves with them.
- The sponsor's number and the team's differ by 203.67 hours, about $16,737. Either the slice gets smaller or the timeline gets longer; that decision is the team's, to be recorded in the change log when it is made.
- The sponsor confirmed on 5 October 2026 that a Business Case and an ROI Analysis are not Sprint 2 deliverables; when the course calls for them, this budget is their cost side. The change log records every revision to this page and what it affected.

Delivered by the team: One-Page Budget Summary: the team's summary as delivered, 6 October 2026 (https://gpi-portal.onrender.com/docs/sprint-2-budget-summary.pdf); Building the Budget: the team's completed Session 11 activity, final version of 4 October 2026 (https://gpi-portal.onrender.com/docs/sprint-2-budget.pdf).

Generated from the portal source at build time. The web page and this PDF are two renders of the same document. Revision history: v1.0 (Oct 4, 2026) The team's completed Session 11 activity, 'Building the Budget', carried onto the page as written, with the delivered file as the Team's PDF. The nine charts are redrawn from the team's figures in the portal's palette. Two things in the delivered file are not carried: a line left over from an earlier draft in the cost-baseline cell of the first table ($42,051, with $37,219 over three months and a $2,103 cushion), which the rest of the document supersedes, and two spacing slips in the figures $49,622 and $21,381. The template's Slice and Status fields, blank in the delivered file, are not shown. No figure changed.; v1.1 (Oct 5, 2026) The team's final file replaces the first as the Team's PDF: the Slice and Status fields are filled and the leftover line is gone, and the sheet at the top of the page now shows the slice and the status. The team's one-page budget summary of 6 October 2026 is added as the opening section, the sponsor's view, and as a second Team's PDF, with its effort-range chart redrawn in the portal's palette. The two spacing slips in the figures $49,622 and $21,381 remain in the ten-step file and are still written as figures here. No figure changed.; v1.2 (Oct 5, 2026) The closing note no longer announces a Business Case and an ROI Analysis for this sprint, after the sponsor's confirmation of 5 October 2026, and points to the change log. No figure changed.; v1.3 (Oct 5, 2026) Owner assigned: Emmanuel Saenz, Project Manager, as the budget's own table has the cost baseline built by the project manager and the contingency under the project manager's control. No content change.
